

Site Register Book

PAGE 003

DATE: / /

and
Sample Register Book
Date: 09/08/22

Location: Tree Park

Work: ① Dismantling of chain link Fencing

Date: 10/08/22

Location: Tree Park

Work: ① Earthwork for SSM

Date: 11/08/22

Location: Tree Park

Work: ① Earthwork for SSM

Date: 13/08/22

Location: Tree Park

Work: ① Laying of WMM

Date: 14/08/22

Location: Tree Park

Work: ① 88mm Size Stone Masonry

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Date: 15/08/22

location: Tree Park

work: ① Size Stone Masonry work

Date: 16/08/22

location: Tree Park

work: ① Size Stone Masonry work

Date: 17/08/22

location: Tree Park

work: ① Size Stone Masonry work

work: ① Size Stone Masonry work

Date: 18/08/22

location: Tree Park

work: ① Size Stone Masonry work

Date: 19/08/22

location: Tree Park

work: ①

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92/

Date 20/08/22

Location : Tree park

Work : size stone Masonary works

Date 22/08/22

Location : Tree park

Work : SSM work

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Date 23/08/22

Location : Tree park

Work : size stone Masonary work

Date : 24/08/22

Location : Tree park

Work : size stone Masonary work

Date : 25/08/22

Location : Tree park

Work : SSM work

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Date : 26/08/22

Location : Tree park

Work : SSM work

Date : 27/08/22

Location : Tree park

Work : SSM work

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Date : 28/08/22

location : Tree Parks

work done : Copping Concrete Laying

Date : 29/08/22

location : Tree Parks

work done : Copping Concrete Laying
+ Pole Fixing

Date : 30/08/22

location : Tree Parks

work done : Copping Concrete Laying
+ Pole fixing + Enroll fixing

Date : 01/09/22

location : Tree Parks

work done : Copping Concrete Laying

→ Pole fixing + Enroll fixing

Date : 05/10/22

location : Basaveswara Parks

Work done : Dismantling chain link fence

Date : 15/10/22

location : Basaveswara Parks

Work : Earth works, Excavation

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 9

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 9

17/10/22.

Location: Baraveshwara hill, Baraveshwara park

Work: ① SSM work for Park
② Stone pitching work for Kalyani.

Date: 18/10/22

Location: Baraveshwara Hills, Baraveshwara Park

Work:

① SSM work for Park
② Stone pitching work for Kalyani

Date: 19/10/22


Location: Baraveshwara Hills, Baraveshwara Park

Work: ① SSM work for Park
② Stone pitching work for Kalyani

Date: 20/10/22

Location: Baraveshwara Hills, Baraveshwara Park

Work: ① SSM work for park
② Dismantling of chain link fencing
③ Earthwork for SSM for Park
④ Stone pitching work for Kalyani


Asst. Executive Engineer
Project Division
Yelahanka Zone
BMP, Bangalore - 92

21/10/22

location :- Basaveshwara Hills, Basaveshwara Park

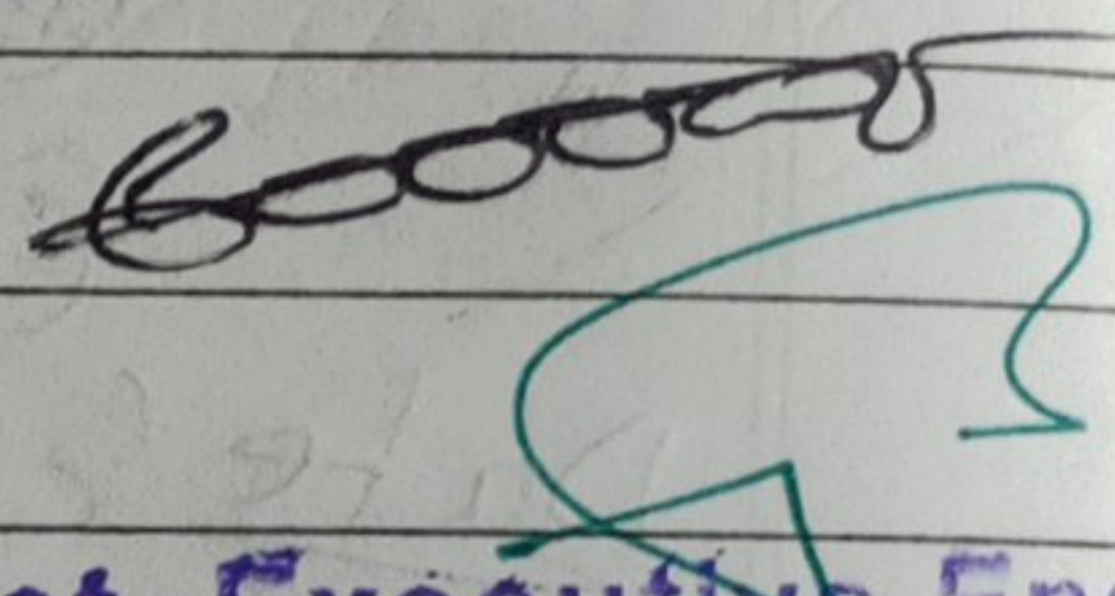
- work:
- ① SSM work at Park
 - ② Stone pitching work for Kalyani

Date: 24/10/22

location :- Basaveshwara Hills, Basaveshwara Park

- work:
- ① SSM work at Park
 - ② Stone pitching work for Kalyani

Date: 27/10/22


Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

location :- Basaveshwara Hills, Basaveshwara Park

- work:
- ① capping work at Park
 - ② Painting work at Park
 - ③ Stone Pitching work at Kalyani.

Date: 28/10/22

location :- Basaveshwara Park, Kalyani Park

- work:
- ① capping work at Park
 - ② Painting work at Park
 - ③ Stone pitching work at Kalyani

Date: 31/10/22

Location: Basaveshwara Park, Kalyani work
Tree Parks

- Work:
- ① SSM work at Park
 - ② Stone Pitching work at Kalyani
 - ③ Gril painting works.

Date: 2/11/22

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 56

Location: Basaveshwara Park, Kalyani work

- Work:
- ① SSM work at Park
 - ② Painting work
 - ③ Stone Pitching at Kalyani

Date: 8/11/22

Location: Basaveshwara Park, Kalyani work
Netaji Park.

- Work:
- ① Pole fixing work at Park
 - ② Stone pitching work at Kalyani
 - ③ Earthwork at Netaji Park.

Date: 11/11/22

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Location: Netaji Park, Kalyani work

- Work:
- ① SSM work at Netaji Park
 - ② Stone pitching work at Kalyani

Date : 14/11/2022

Location : Netaji park, Basaveswara hill

Work : SSM work + pole fixing

Date : 15/11/2022

Location : Netaji park, Basaveswara park, Someshwara hill, BBMP, Bangalore-02

Work : ① painting work at Basaveswara park

② ~~SSM~~ SSM work Netaji park

Date : 16/11/2022

Location : Netaji Park, Basaveswara park, Someshwara hill

Work : ① Copping Concrete at Netaji park
② site inspection by QA Sir, AE Sir

Date : 17/11/2022

Location : Netaji park

Work : SSM work, pole fixing

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-02

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-02

Date: 18/11/22

Location: Netaji park

work: SSM work

Date: 19/11/22

Location: Netaji park

work: SSM work

Date: 28/11/22

Location: Someshwara hill, Netaji park

work: Kerb laying, Copping concrete laying

Date: 29/11/22

Location: Kalyani

work: Kerb laying

Date: 30/11/22

Location: Kalyani

work: Kerb laying

Asst. Executive Engi
Project Division
Yelahanka Zone
BBMP, Bangalore
